



0


La Brea Subarea Updates Public Works Commission November 10, 2022














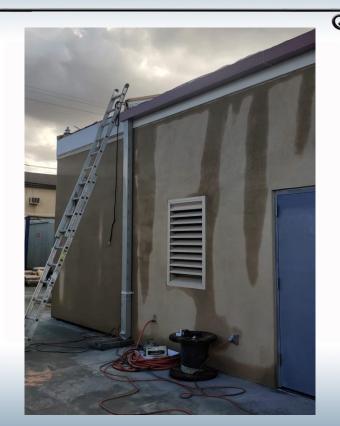

Rain Gutters & Roofing





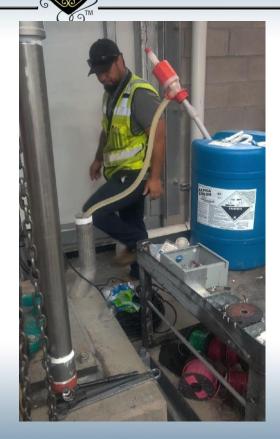







Well Chlorination





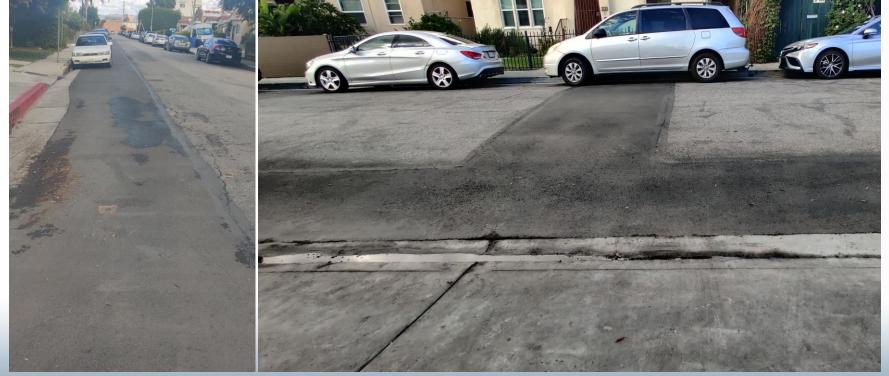

Final Paving



a Brea Subarea Overview

0

LCW NO. 1 - EQUIPPING

- Budget: \$2,900,000
- Work Billed: \$2,710,391
- Percent Work Complete: 99%
- Extra Work: Disinfect transmission main on 11/20/22

LCW No. 2 & 3 - DESIGN

- Proposal received
- Approval of design contract scheduled for 12/6/22



La Brea Subarea Development Project Timeline

